


Actual Work
 Remaining Work
 Milestone
 Summary



█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

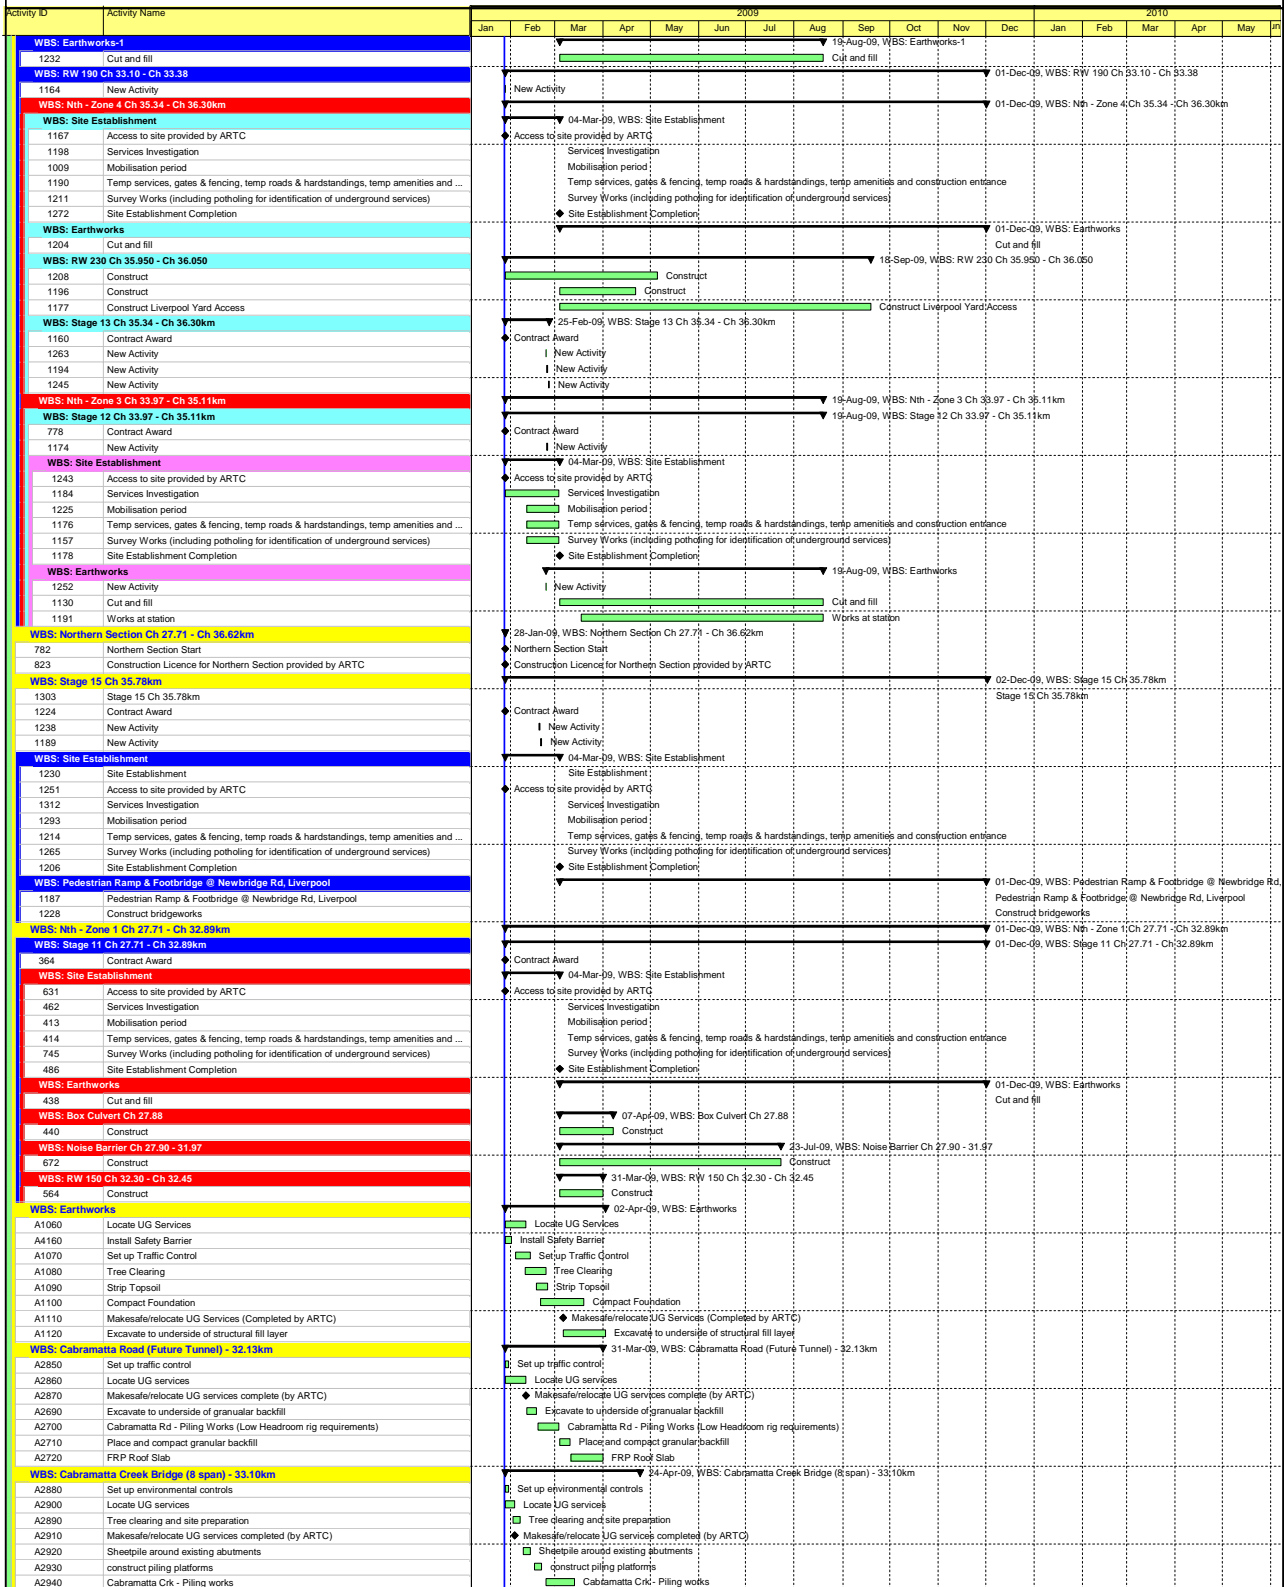

Activity ID	Activity Name	2009												2010						
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
A2950	FRP Pile Caps (9 no.)																			
WBS: Station works at Sefton and Carramar		▼ 08-Apr-09, WBS: Station works at Sefton and Carramar																		
WBS: Carramar Station Works		▼ 08-Apr-09, WBS: Carramar Station Works																		
WBS: Pre-Construction		▼ 08-Apr-09, WBS: Pre-Construction																		
412	Receive full construction drawings	Receive full construction drawings																		
424	Services Search	Services Search																		
405	Survey	Survey																		
423	Establish site	Establish site																		
417	Order Pre-cast underpass extensions	Order Pre-cast underpass extensions																		
408	Order 250mm infill Precast walls	Order 250mm infill Precast walls																		
406	Relocation of services (By ARTC)	Relocation of services (By ARTC)																		
WBS: Footing Works - East Side		▼ 16-Mar-09, WBS: Footing Works - East Side																		
410	Erect hoardings on east side	Erect hoardings on east side																		
421	Demolish east side wall and floor	Demolish east side wall and floor																		
422	Excavation	Excavation																		
433	Blinding	Blinding																		
434	Footing reo and concrete	Footing reo and concrete																		
415	Installation of new drainage	Installation of new drainage																		
416	Cast slab over existing drainage pit	Cast slab over existing drainage pit																		
427	Cut and drill into existing wingwall	Cut and drill into existing wingwall																		
418	Remove hoardings on east side	Remove hoardings on east side																		
WBS: Footing works - West side		▼ 07-Apr-09, WBS: Footing works - West side																		
420	Erect hoardings on West side	Erect hoardings on West side																		
431	Demolish west side wall and floor	Demolish west side wall and floor																		

Actual Work ◆ Milestone
 Remaining Work ▼ Summary
