



SSFL Overview
Fairfield Community Liaison Group

Action Items from previous meeting:

1. The gates were open opposite 120 and 150 Broomfield Street, Cabramatta.

SF Safety Manager investigated on 3 March and found that the gates were RailCorp's gates into the rail corridor and had since been closed.

2. What risk or contingency management plans are in place for the Broomfield Street Sewer Works?

The 3A Rail Project Manager will update the CLG members in this meeting.

Woodville Road to Bareena Street

- Concrete type F barrier and galvanised W bean crash barrier works on Villawood Road (on top of the Blue Circle area) are on hold awaiting detailed design.
- Completing the remaining works on retaining walls RW120 and RW115.
- Temporary fencing is to be removed around the Carramar Station underpass once these two retaining walls are complete.
- Continuing site maintenance in April including grass cutting, environmental and fencing repairs.
- Installing the main cable route.

Cabramatta Station

- Station work is continuing with work to the platforms.
- Carparking at Area 5 on Railway Parade has commenced and will be completed late May 2011 including completion of the retaining wall.
- Paving and kerbing to be undertaken after completion of the Broomfield Street Sewer Diversion Works.

Broomfield Street, Cabramatta - the works will involve localised micro-tunnelling, excavation and trenching.


Programme

Proposed start date 1 May 2011 with completion scheduled for September 2011 (20 weeks).

Breakdown

- Mobilisation and potholing for services (1 week)
- Construction of exit and entry pits (4 weeks)
- Micro tunnelling East of Fisher St (3 weeks)
- Micro tunnelling West of Fisher St (5 weeks)
- Open cut trench works at Bridge St end (2 weeks)
- Backfill, bitupave and reapply line marking (1 week)
- Connections with existing services (2 weeks)
- Demobilisation and 'make-good' works (2 weeks)

- ARTC, 3A Rail and Stations First personnel have met with Council to review the construction program.
- The traffic control plan submitted to Council has been approved.
- Traffic controls will be in place to manage vehicular movements.
- Pedestrian access will be maintained at all times.
- A number of parking bays on Broomfield Street along the construction route will be unavailable throughout the different stages of the work to enable two lanes of traffic to remain open.
- Parking bays will remain open around the station in adherence to council requirements.
- The community have been notified adhering to notification timeframes and guidelines.

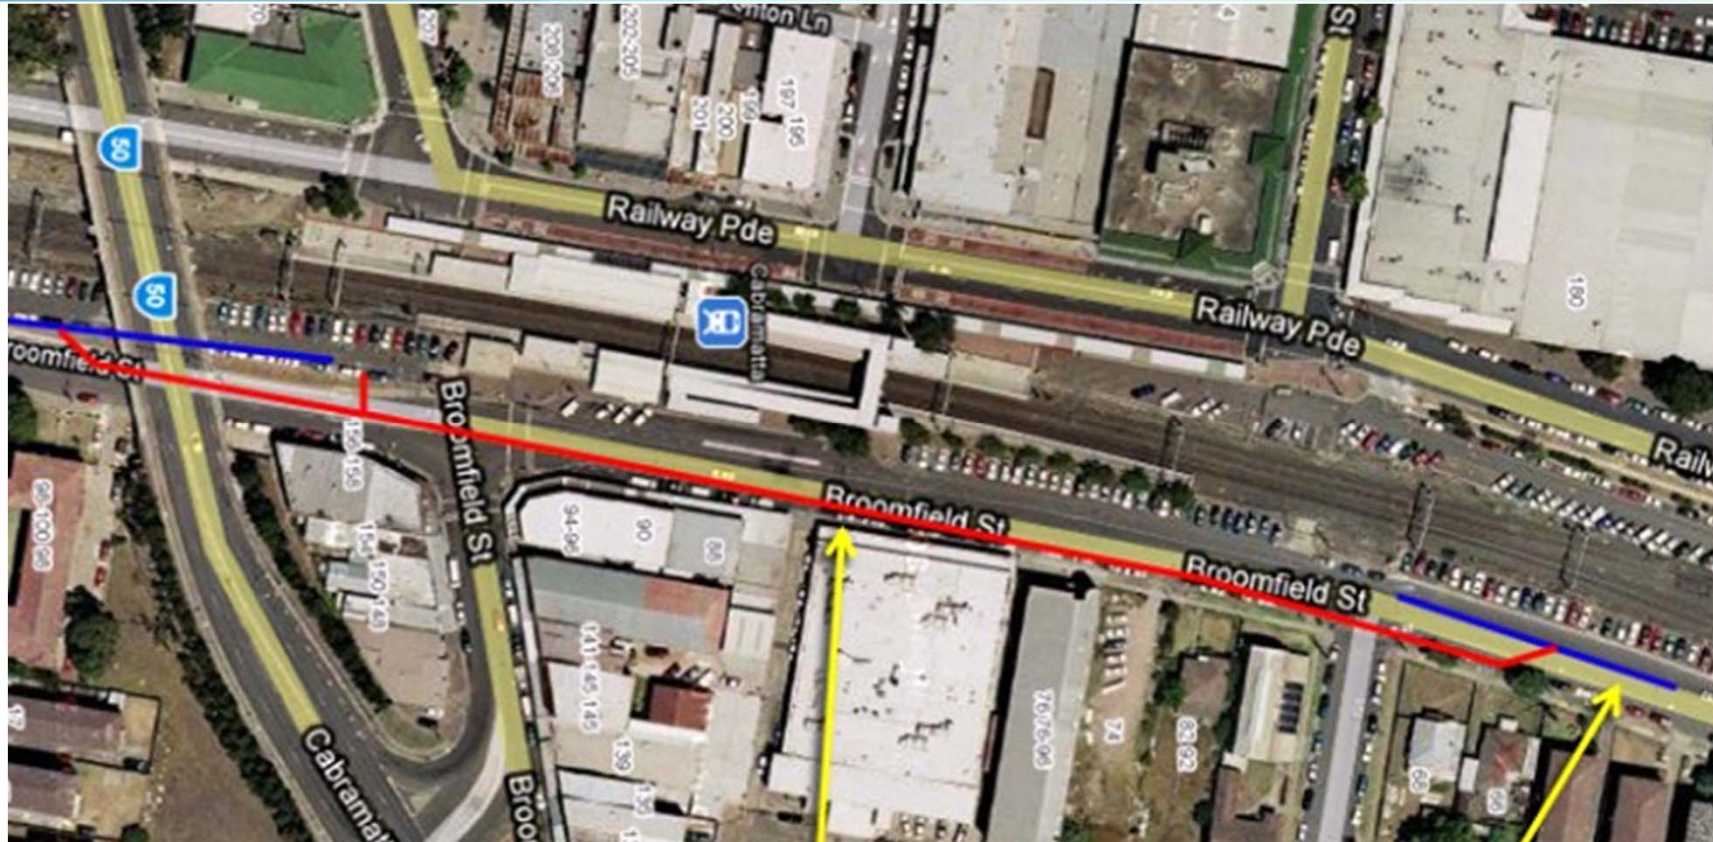

Proposed
Adjustment

Existing
Sewer

Out of Hours Work

Weekend 46: 14 to 15 May

Location of Works: Cabramatta Station.

Time: 7am to 6pm Saturday 14, and 8am to 6pm Sunday 15 May 2011. A contingency is in place from 6pm to 10pm both days.

Activity: Back of platform works including widening the platform, installing the new awning and undertaking electrical modifications.

Equipment: Delivery truck, oxy sets, 60t crane, 20t Franna, scaffolding, elevated work platform, and powered and non-powered hand tools.

- CLG's
- Letterbox drops
- Individual briefings (only in noise sensitive areas as defined by the noise report)
- Respite Offers (only in noise sensitive areas as defined by the noise report)
- Alternate Accommodation (only in noise sensitive areas as defined by the noise report)



General Business

Next meeting:

Wednesday 4 May 2011

- Complaints Hotline: 1800 182 543
- Email address: ssfl@artc.com.au
- Website: www.ssfl.artc.com.au
