



SSFL Overview
Liverpool/Campbelltown Community Liaison Group

- Construction of station proper going well
- The stairs will be erected prior to the ramp recess and lift erection. This should avoid any discomfort to commuters and community
- RailCorp will be establishing a worksite so they can carry out their works - they are building a new ticket office
- Bike lockers are being completed - 3 outstanding
- Minto car park works is on schedule and by the next CLG should be close to completion
- Work this weekend - lift frames will be erected on each side; the middle frame will be installed at a later date

- Suspension has been lifted on Warwick Farm Station
 - Site establishment completed
- There will be padmount transformers installed at both Warwick Farm and Casula, in the next month
- Notifications will be delivered to all community members
- Car parking spaces will be reclaimed to enable lift construction

Casula Station

- It is anticipated that construction at Casula Station will recommence in the near future.

Leumeah Station

- Contractor will be re-establishing site before next CLG

Liverpool Compressor Hut

Earthwork in preparation for the foundation on hut- commenced


Civil works for power supply

Lifting the prefabricated building (20t)



Cable Route Construction

- Potholing, civil works, excavation and installing conduits for signalling & comms

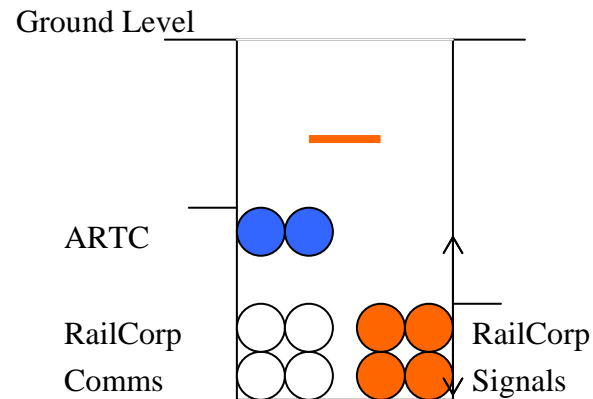

Glenfield works in conjunction with GJA

- Relocate GD4 signal to new position and associated signalling equipment
- Relocate 10BT Feed, 10AT Feed
- Relocate signal from gantry to post
- Construct new cable route
- Relocate Rail Temperature Sensor



Casula/Glenfield Ck - Poles and Aerials

- Works: Installation of new power poles and aerials.
- Plant and equipment: Bucket trucks, cranes, pole truck and light vehicles.
- Environment: Minimal impact. Lane closures adjacent to Casula Powerhouse on 3/7/10 & possibly 10/7/10 will be controlled by traffic controllers. TCP attached. Noise levels kept well below normal acceptable levels.

Casula/Glenfield Underground Cable Install

- Works: Installation of 33kv underground cable and jointing works.
- Plant and Equipment: cable drum turner, cable winch and light vehicles.
- Environment: Minimal impact. Noise levels kept well below normal acceptable levels.

Liverpool Turnback Poles and Aerials

- Works: Installation of new power poles and aerials.
- Plant and equipment: Bucket trucks, cranes, pole truck and light vehicles.
- Environment: Minimal impact. Noise levels kept well below normal acceptable levels.

Water Crossing 43

- Concrete encasement of a DN750 water main, north of Terminus St, Liverpool Station.
- Concrete encased water main to be laid via open trenching. Run extends from Liverpool Station and approx. 40m down the embankment.
- Anticipated start mid July. Duration 3 weeks.

Sewer Reline Crossing 49

- Relining of DN225 sewer main in the Mills Park area.

Sewer Reline Crossing 64

- Relining of DN225 sewer main, north of Campbelltown Rd.

ODG to manage relining contractor Interflow

- Sewer relining is a low impact activity which occurs between two Syd Water manholes on each side of the tracks. A membrane is fed into the sewer main and mechanically unwound to seal the wall of the sewer main. The process takes half a day with a small truck and traffic diversion around each manhole if required. Anticipated start mid July. Duration 1 day.

Sewer main diversion and water main ULX at Glenfield Rd x53 & x54

- Ongoing pipe laying works and backfilling of trench along Glenfield Road and in vicinity of Glenfield substation. Anticipated completion in 1 month.

ULX 62 Leumeah Station

- Ongoing Syd Water pipe laying works anticipated completion 2 weeks time.

Water and sewer main Diversion Crossing 70 & 70a at Farrow Rds

- Main works completed and backfilled. Minor Domestic connection works will be ongoing for 2-3 weeks.

- Continuation of channel diversion & earthworks in the Glenfield area

A site compound will be set up in the rail corridor south of Macarthur Station off Menangle Road, south of Glen Alpine Drive roundabout.

This will be set up from 24th May 2010 until the end of August 2010.



Out of Hours Work

Liverpool South (ODG)

7.00am until 5.00pm both Saturday and Sunday

Activity: Construct underground cable route

Equipment: Excavator, dump truck, light vehicle, hand tools, 10 people

Shepherd Street Bridge, Liverpool (LOR)

7.00am until 6.00pm both Saturday and Sunday

Activity: Liverpool Section Hut - commissioning and integration into RailCorp Infrastructure

Equipment: hirail trucks, elevated work platforms

Casula - Glenfield Flyover

08.00am until 23.59 Saturday 19th June 2010 and 00.00 to 22.00 Sunday 20th June 2010

Activity: Foundation treatment works (piling) and construction of retaining walls and earthworks

Equipment: Excavators, rollers, graders, tipper trucks, bobcats, forklift trucks, water trucks, knuckle booms, working platforms, hand tools, lighting towers.

Casula to Glenfield (ODG)

7.00am until 5.30pm both Saturday and Sunday

Activity: Changeover signalling cables, relocation of signals, removal of cross over, installation of cable pits

Equipment: Light vehicle, excavator, hand tools and 10 people

Glenfield Tie-In

08.00am until 11.59pm Saturday 19th June 2010

00.00 until 10.00pm Sunday 20th June 2010

Activity: Earthworks, construction of drainage works and installation of CSR route

Equipment: Excavators, rollers, graders, tipper trucks, bobcats, forklift trucks, water cart, knuckle booms, working platforms, hand tools, lighting towers, boggies, truck and dog, concrete truck and concrete pump

Ingleburn

7.00am until 5.00pm on both Saturday and Sunday

Activity: Overhead wiring - footing installation and removal

Equipment: 2 x cranes, 2 x manitous

Minto to Ingleburn

7.00am until 6.00pm on both Saturday and Sunday

Activity: Relocation of IN 22 Signal Location

Equipment: Excavator, non-destructive high pressure blaster and vacuum plant (sucker truck), tippers and lighting tower

Minto to Ingleburn

7.00am until 6.00pm on both Saturday and Sunday

Activity: Relocation of IN 24 Signal Location

Equipment: Site vehicles, excavators, non-destructive high pressure jet blaster and vacuum plant (sucker truck), tippers, sites to contain approximately 20 workers daily

Minto Station

Saturday 02.00am until Monday 02.00am

Activity: Fit bridge components, fit cladding to lift shifts, fit handrails, carry out demolition works to existing ramp structure and power upgrade

Equipment: 100t crane, 20t franna crane, scaffold, scissor lift, hand tools, delivery trucks, oxy sets, traffic management and generator

Campbelltown Yard Track Works

6.00am until 8.00pm on both Saturday and Sunday

Activity: Remove perway siding

Equipment: 2 x front end loaders, rail saw, semi trailer, small hand tools, 16t hand excavator, 1 x water cart, 1 x street sweeper

Campbelltown

Saturday 02.00am until Monday 02.00am

Activity: Resurface area of platform adjacent to the stair no 3, carry out adjustments to the bridge

Equipment: 20t franna, hand tools, delivery trucks, oxy sets and generators

Campbelltown

7.00am until 5.00pm on both Saturday and Sunday

Activity: Removal of pole stumps at Farrow Road and Hurley Street
Campbelltown

Equipment: stump grinder, site vehicle

Campbelltown Yard

6.00am until 6.00pm on both Saturday and Sunday

Activity: New signalling installation works, pot holing of existing buried cable routes, excavating cable route trenches, installation of underline crossings

Equipment: site vehicles, excavators, non-destructive pressure jet blaster and vacuum plant, tipper trucks, dump trucks and bobcat

Macarthur Tie-In

08.00am until 11.59pm on Saturday

00.00 until 10.00pm on Sunday

Activity: Earthworks, construction of drainage works, tie in to existing capping and installing bridge girders

Equipment: excavators, rollers, graders, tipper trucks, bobcats, forklift trucks, water cart, knuckle booms, working platforms, hand tools, lighting towers, bogies, truck and dog, concrete trucks, concrete pump

Macarthur

7.00am until 5.00pm on both Saturday and Sunday

Activity: New Signalling Installation Works: pot holing of existing buried cable routes, excavating cable route trenches, installation of under line crossings

Equipment: Site vehicles, excavators, non-destructive high pressure jet blaster and vacuum plant, dump trucks and bobcat

Macarthur/SSFL Installation Works

7.00am until 5.00pm on both Saturday and Sunday

Activity: New Signalling Installation Works: pot holing of existing buried cable routes, excavating cable route trenches, installation of under line crossings

Equipment: Site vehicles, excavators, non-destructive high pressure jet blaster and vacuum plant, dump trucks and bobcat

Weekend 05 - 31st July til 1st August Out of Hours Activities

Warwick Farm Station (Hume Highway Bridge)

7.00am until 5.30pm on both Saturday and Sunday

Activity: Install cable tray

Equipment: Hand tools, ladder, generator

Weekend 05 - 31st July til 1st August Out of Hours Activities

Warwick Farm Station

Time: TBA

Activities: Power upgrade, demolition of existing waiting room, works to platform and bridge, installation of awning, installing of lift shafts

Equipment: 30t excavator, demolition tools, pulveriser, jack hammers, oxy sets, dump trucks, compactors, scaffold, 250t crane, hi-rails(x2)



Weekend 05 - 31st July til 1st August Out of Hours Activities

Shepherd Street Bridge, Liverpool

7.00am until 6.00pm on both Saturday and Sunday

Activities: Liverpool Section Hut - Commissioning and Integration into RailCorp Infrastructure

Equipment: HiRail Trucks, Elevated Work Platform

Weekend 05 - 31st July til 1st August Out of Hours Activities

Casula Station

Time: TBA

Activity: Installation of lift shaft

Equipment: 60t crane, scissor lifts, scaffold



Weekend 05 - 31st July til 1st August Out of Hours Activities

Glenfield

2.00am Saturday until 2.00am Monday

Activities: Straight line crossover, tamp and adjust

Equipment: Tamper and regulator, 1 x 16t dumpers, 2 x front end loaders, drott

- CLG's
- Letterbox drops
- Individual briefings (only in noise sensitive areas as defined by the noise report)
- Respite Offers (only in noise sensitive areas as defined by the noise report)
- Alternate Accommodation (only in noise sensitive areas as defined by the noise report)

Any question on the Out of Hours Works?

General Business

Next meeting:

Wednesday 21st July 2010

- Complaints Hotline: 1800 182 543
- Email address: ssfl@artc.com.au
- Website: www.ssfl.artc.com.au
