



*SSFL  
OOH Works scheduled for  
December 2011 and January 2012  
Liverpool LGA and Campbelltown LGA*



Dear Liverpool/ Campbelltown CLG Members

In accordance with our Environment Protection Licence (EPL) we would like to notify you with an update on proposed SSFL out of hours (OOH) works for December 2011 and January 2012 in your LGA's.

SSFL has applied to the Office of Environment and Heritage (OEH) to utilise the RailCorp track possession weekend on 17 - 18 December 2011 and the RailCorp January close down period from 3-20 January 2012.

These OOH works will also be presented at the combined CLG meeting on 7 December 2011.

RailCorp has a track possession scheduled on 17 and 18 December 2011 and a January Closedown from 2 January to 22 January 2012, which will be utilised by the Southern Sydney Freight line to undertake work safely.

OOH in December 2011 and January 2012 are scheduled for:

- December RailCorp Possession - 17/18 December 2011
  
- January RailCorp Close Down
  - 7/8 January 2012
  - 14/15 January 2012
  - 21/22 January 2012
  
- Non-possession OOH - various weekends until 31 March 2012



**Location of Works: Woodville Rd, Villawood to Liverpool Hospital**

**Time:** From 6pm to 10pm on weeknight evenings from Tuesday 3 January to Friday 20 January, and from 7am to 6pm on Saturdays and from 8am to 6pm on Sundays on the weekends of 7-8, 14-15 and 21-22 January 2012.

**Activity:** Potholing, earthworks, surveying and tree removal works

**Equipment:** Light vehicles, trucks, lighting towers, generators, a potholing truck, bogies, grader and drott, 20t excavators, 13t excavator, rollers, compactor plates, chainsaws, chipper, stump grinder, 100t mobile crane, 20t franna, water cart, and powered and non-powered hand tools.

**Location of Works: Broomfield Street, Cabramatta to Liverpool Hospital, Liverpool**

**Time:** From 6pm to 10pm on weeknight evenings from Tuesday 3 January to Friday 20 January, and from 7am to 6pm on Saturdays and from 8am to 6pm on Sundays on the weekends of 7-8, 14-15 and 21-22 January 2012.

**Activity:** Excavation and installation of noise wall posts and panels, drainage and cabling works

**Equipment:** Small excavator and bob cat, piling rig, concrete agitator truck, concrete pump, 20t franna, elevated work platform, sucker truck, generators, compressor, jack hammer, demolition saw, lighting towers, 30t trench digger, hi-rail, excavators, 10t dumper, backhoe, trucks, 2t hino tipper truck, and powered and non-powered hand tools.

**Location of Works: Boundary Lane, Cabramatta to Hume Hwy, Warwick Farm**

**Time:** From 6pm to 10pm on weeknight evenings from Tuesday 3 January to Friday 20 January, and from 7am to 6pm on Saturdays and from 8am to 6pm on Sundays on the weekends of 7-8, 14-15 and 21-22 January 2012

**Activity:** Modifications to existing signal pits

**Equipment:** 20t excavator, lighting tower, compressor and jack hammer, and powered and non-powered hand tools.



## *OOH Works -Various non-possession*

### **Location of Works: Warwick Farm Station**

**Time:** From 7am to 6pm on Saturdays and from 8am to 6pm on Sundays on the weekends of 7-8, 14-15 and 21-22 January 2012. A contingency is approved from 6pm to 10pm on all days worked from Tuesday 3 January to Friday 20 January 2012

**Activity:** Station works, including demolition of existing waiting room, power upgrade works, remedial bridge works, platform works, and back of platform works

**Equipment:** 20t franna, delivery vehicles, mobile scaffold, elevated work platform, knuckle boom, oxy set, jackhammer, concrete saw, rattle guns, compressor, generator, concrete pump, and powered and non-powered hand tools.

### **Location of Works: Shepherd Street, Liverpool to Casula Powerhouse**

**Time:** From 7am to 6pm Saturday and from 8am to 6pm Sunday on the weekends of 17-18 December 2011 and 7-8, 14-15, and 21-22 January 2012.

**Activity:** Casula Access Road works, including clearing, earthworks, bulk earth movement, construction of retaining walls (including piling), shotcreting and anchoring, culvert works, drainage works, maintenance of access ramps and cycleway works, as well as high voltage works, including installation and removal of power poles with associated aerial works

**Equipment:** pole trucks, elevated work platforms, excavators, compactors, rollers, bobcats, cranes, frannas, water cart, piling rig, trucks, dump trucks, concrete trucks, rollers, graders, boom pumps, anchoring rigs, generators, compressors, hydraulic hammers, and powered and non-powered hand tools.

### **Location of Works: Casula Station**

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 17-18 December 2011 and 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Saturday 17 and Sunday 18 December 2011, and on all days worked between Monday 2 January and Sunday 22 January 2012.

**Activity:** Station works, including bridge works, the extension of the deflection wall, works to lift shafts, platform works and a power upgrade

**Equipment:** A 100t crane, 20t franna, mobile scaffolding, elevated work platform, knuckle boom, concrete pump, generator, high rail, piling rig, and powered and non-powered hand tools.

**Location of Works:** Casula Station to Glenfield Tip

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on one weekend between Saturday 17 December 2011 and Sunday 22 January 2012

**Activity:** Removal of redundant power poles

**Equipment:** A pole truck, two mobile cranes, an elevated work platform, and powered and non-powered hand tools.


**Location of Works:** Casula Station to Glenfield

**Time: Area A+C:** From 6am to 6pm Saturday and 6am to 10pm Sunday on the weekends of 17-18 December 2011 and 7-8, 14-15, and 21-22 January 2012.

**Area B:** From 6am Saturday 17 December to 10pm Sunday 18 December and between 6am Tuesday 3 January to 10pm Sunday 22 January 2012

**Activity:** Piling, retaining wall construction, earthworks, drainage works, installation of temporary access roads and level crossing, potholing, installation of flyover hoarding panels and concrete blocks, as well as overhead wiring works

**Equipment:** A 5t excavator, 8t tipper, two elevated work platforms, a pothole truck, piling rigs, excavators, truck & dogs, 100t crane, concrete trucks, concrete pumps, vibratory rollers, lighting towers, portable generators, and powered and non-powered hand tools.

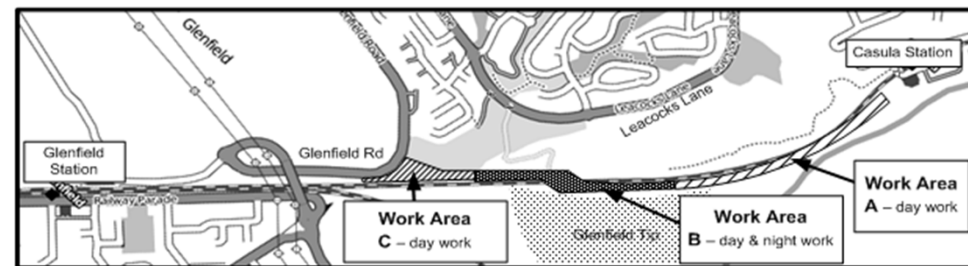



## *OOH Works -Various non-possession*

**Location of Works: Glenfield Road, Glenfield**

**Time:** From 7am to 6pm on Saturday 17 December and from 8am to 6pm on Sunday 18 December 2011. An approved contingency is in place from 6pm to 10pm on both days.

**Activity:** Survey and set up work, potholing, clearing and the installation of hoarding

**Equipment:** A 5t to 20t excavator, pothole truck, lighting towers, and powered and non-powered hand tools.

**Location of Works: Glenfield Road, Glenfield**

**Time:** from 7am to 6pm on Saturdays and from 8am to 6pm on Sundays on the weekends of 7-8, 14-15 and 21-22 January 2012

**Activity:** Drainage and excavation works, as well as the installation of a temporary work platform

**Equipment:** 5t-10t excavator, mobile crane, front-end loader, excavator, trucks, and powered and non-powered hand tools.

**Location of Works: Freeman Circuit, Ingleburn to Victoria Road, Minto, and Ben Lomond Road, Minto South to Broughton Street, Campbelltown**

**Time:** From 7am Saturday to 6pm Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Sunday evenings on 8, 15 and 22 January 2012.

**Activity:** Removal of redundant signalling and communication pits

**Equipment:** Light vehicles, 5t-20t excavators, bogie trucks, and powered and non-powered hand tools.

**Location of Works: Chester Road, Ingleburn to Campbelltown Station**

**Time:** From 7am Saturday to 6pm Sunday on the weekends of 17-18 December 2011, and 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Sunday 18 December 2011, 8, 15 and 22 January 2012.

**Activity:** Potholing and surveying works

**Equipment:** Pothole trucks, lighting towers, portable generators, a bobcat and site vehicles.



## *OOH Works -Various non-possession*

**Location of Works:** Sackville Street, Ingleburn to Rose Street, Campbelltown

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 17-18 December 2011, and 7-8, 14-15, and 21-22 January 2012.

**Activity:** Excavation and installation of temporary sheet piles

**Equipment:** A 5t hi-rail excavator, 8t hi-rail tipper, hi-rail pothole truck, vibratory sheet piling rig, truck and dogs, site vehicles, and powered and non-powered hand tools.

**Location of Works:** Memphis Street to Victoria Road, Minto

**Time:** From 7am to 6pm Saturday and 8am to 6pm Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Sunday evening on 8, 15 and 22 January 2012

**Activity:** Minto viaduct concrete works

**Equipment:** Light vehicles, concrete pump, concrete agitator trucks, and powered and non-powered hand tools

**Location of Works:** Victoria Road, Minto to Rose Payton Drive, Leumeah

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 17-18 December 2011, and 7-8, 14-15, and 21-22 January 2012

**Activity:** CCTV installation works

**Equipment:** A CCTV truck, site vehicles and hand tools

**Location of Works:** Stafford Street, Minto and Leumeah Station

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on two weekends out of the following dates; 17-18 December 2011, 7-8, 14-15, or 21-22 January 2012.

**Activity:** Removal of a redundant galvanised steel trough (GST) in the rail corridor

**Equipment:** Excavators, light vehicles and powered and non-powered hand tools.



## *OOH Works -Various non-possession*

### Location of Works: **Minto Station**

Time: From 7am to 6pm on Saturday and 8am to 6pm on Sunday on two weekends out of the following dates; 17-18 December 2011, 7-8, 14-15, or 21-22 January 2012.

Activity: Commissioning of the new compressor hut and isolation transformer, as well as cabling works

Equipment: Site vehicles and hand tools.

### Location of Works: **Minto Station**

Time: From 7am Saturday to 10pm Sunday on the weekends of 17-18 December 2011 and 7-8, 14-15, and 21-22 January 2012.

Activity: Station works, including power upgrade works, back of platform works, demolition of the existing access ramp, concrete pouring, bridge and lift shaft works and concrete works

Equipment: A 200t crane, 20t franna, mobile scaffold, elevated work platform, concrete pump, generator, oxy set, scaffolding, piling rig, hi-rail, k

### Location of Works: **Sussex and Stafford Streets, Minto**

Time: From 7am to 6pm on Saturday and 8am to 6pm on Sunday on one weekend in January or February

Activity: Demolition and removal of the old Minto Compressor Hut

Equipment: Site vehicles, excavators, dump trucks, and powered and non-powered hand tools.

### Location of Works: **Leumeah Station**

Time: From 7am to 6pm on Saturday 17 December 2011. An approved contingency is in place from 8am to 6pm on Sunday 18 December 2011.

Activity: Installation of a walkway over the new culvert extension

Equipment: A 40t crane, and powered and non-powered hand tools.



## *OOH Works -Various non-possession*

### Location of Works: Leumeah Station

Time: From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 17-18 December 2011, and 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on all days worked

Activity: Station works, including bridge works, platform works, service installation, and lift works

Equipment: A 100t crane, 20t franna, scaffolding, elevated work platform, oxy set, electric drill, power saw, generator, knuckle boom, concrete saw, piling rig, concrete pump, high rail, delivery and site vehicles, and powered and non-powered hand tools.

### Location of Works: Leumeah Station

Time: From 7am to 10pm on 17 December 2011 and from 8am to 10pm on 18 December 2011. Three approved contingency weekends are in place from 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012.

Activity: Cabling work and trenching

Equipment: Site vehicles, a concrete saw, angle grinder, plate compactor, and powered and non-powered hand tools.

### Location of Works: Queen Street, Campbelltown

Time: From 7am to 6pm on Saturday 17 December 2011. An approved contingency is in place from 8am to 6pm on Sunday 18 December 2011.

Activity: Placement of precast culvert units into the existing creek

Equipment: A mobile slew crane, 20t franna, semi-trailer truck, 15t excavator, road sweeper, water cart, electrical breaker (for concrete breaking), generator, and powered and non-powered hand tools.

### Location of Works: Queen Street, Campbelltown

Time: From 7am to 6pm on Saturday and from 8am to 6pm on Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Sunday evening on 8, 15 and 22 January 2012

Activity: Cess drain works

Equipment: Light vehicles, excavators, bogie trucks, and powered and non-powered hand tools.



## *OOH Works -Various non-possession*

**Location of Works: Kiabla Street, Campbelltown**

**Time:** From 7am on Saturday 17 December to 6pm on Sunday 18 December 2011. Two contingency weekends are approved from 7am Saturday to 6pm Sunday in January 2012.

**Activity:** Removal of temporary shoring

**Equipment:** a hi-rail excavator, oxy-acetylene set, 2t tipper, and powered and non-powered hand tools. A rail tamper and regulator will be used if required.

**Location of Works: Broughton Street, Campbelltown to Menangle Road, Macarthur**

**Time:** From 7am Saturday to 6pm on Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on Sunday evenings on 8, 15 and 22 January 2012

**Activity:** Potholing, drainage works and temporary works, including the installation of temporary piles and panels

**Equipment:** light vehicles, excavators, bogie trucks and powered and non-powered hand tools.

**Location of Works: Campbelltown Station**

**Time:** From 7am to 10pm on Saturday 17 December and from 8am to 10pm on Sunday 18 December 2011. Two approved contingency weekends are in place from 7am Saturday to 6pm Sunday, on either 7-8, 14-15, or 21-22 January 2012.

**Activity:** Construction of a cable route, hauling of cabling and installation of a concrete slab

**Equipment:** A concrete truck, tip truck, excavator, and powered and non-powered hand tools.

**Location of Works: Campbelltown Station**

**Time:** From 7am to 6pm on Saturday and from 8am to 6pm on Sunday, on 17-18 December 2011, and on 7-8, 14-15 and 21-22 January 2012. An approved contingency is in place from 6pm to 10pm on all days worked.

**Activity:** Staff footbridge works and works under the existing pedestrian bridge, including piling, deflection wall works and installation of structural steel components

**Equipment:** A 100t crane, 20t franna, scaffolding, mobile elevated work platforms, concrete pump, oxy set, power saw, electric drill, generator, concrete saw, piling rig, high rail, knuckle boom, concrete vehicles, delivery vehicles, and powered and non-powered hand tools.



## *OOH Works -Various non-possession*

**Location of Works:** Farrow Road, Campbelltown

**Time:** 48 hours of continuous work between 17 December 2011 and 29 February 2012. An approved contingency is in place for a second 48 hours within the same time period.

**Activity:** Relocation of a pad mount within the property boundary of Campbelltown Frames and Trusses on Farrow Road, Campbelltown

**Equipment:** A 7t excavator, 2t tipper, concrete truck, concrete saw, generator, lighting towers, wacker pack, concrete vibrator, and powered and non-powered hand tools.

**Location of Works:** Hurley Street, Campbelltown

**Time:** from 5am Saturday to 11pm Sunday on the weekends of 7-8, 14-15, and 21-22 January 2012.

**Activity:** Construction of concrete walkways and light pole installation

**Equipment:** Light vehicles, concrete agitators and vibrators, a concrete saw, 13t excavator (contingency only), and powered and non-powered hand tools.

- CLG's
- Letterbox drops
- Individual briefings (only in noise sensitive areas as defined by the noise report)
- Respite Offers (only in noise sensitive areas as defined by the noise report)
- Alternate Accommodation (only in noise sensitive areas as defined by the noise report)

- 24 Hour Information Line: 1800 182 543
- Email address: [ssfl@artc.com.au](mailto:ssfl@artc.com.au)
- Website: [www.ssfl.artc.com.au](http://www.ssfl.artc.com.au)
